



# Completion Certificate

Name of RHD Office : Pabna, (Division Office)  
Name of Contractor : Dhrubo Construction Ltd.  
Name of Contract : Construction of 173.74 m. long (2x30.50m. +3x36.60m.)  
PC Girder Nimai Bridge (Dharma Gacha Ghat) &  
Approach road at 8th km of  
Chatmohor-Handial-Hamkuria road under Road  
Division, Pabna during the year 2014-2015  
Contract Number : e-GP/RJZ/ADP/03/2014-2015(Re-Tender)  
Name of Project : Development of Chatmohar - Handial - Hamkuria Road  
(05139)  
Budget Head : Development  
Value of Contract : Tk.171,934,362.39(seventeen crore nineteen lac thirty-four  
thousand three hundred sixty-two taka and thirty-nine  
paisa only)  
Value of Work Done : TK. 171,870,732.19 (seventeen crore eighteen lac seventy  
thousand seven hundred thirty-two taka and nineteen paisa  
only)  
Commencement Date : 27 October 2015  
Planned Completion Date : 30 June 2016  
Actual Completion Date : 29 June 2016

Certified that the Contractor has completed execution of the works of the contract as mentioned in this Certificate, based on the final measurement recorded in CMS on 30 June, 2016.

Signature of Engineer : *Haidy*  
Name of Engineer : (মোফাজ্জল হায়দার)  
পরিচিতি নং- ৬০১৯৬৬  
Designation of Engineer : নির্বাহী প্রকৌশলী, সওজ  
সড়ক বিভাগ, পাবনা।  
Date of Signature :  
Seal of the Office :

Signature of Contractor : *[Signature]*

Signed  
*[Signature]*

কাজী আব্দুল্লাহ আল-মামুন  
প্রোগ্রামার  
পটক পরিদপ্তর ও মহাপ্রকল্প বিভাগ  
সড়ক পরিবহন ও সেতু মন্ত্রণালয়  
গণপ্রজাতন্ত্রী বাংলাদেশ সরকার



# Completion Certificate

Name of RHD Office : Pabna, (Division Office)

Name of Contractor : Mir Shariful Alam & M/S. Dhrubo construction JV

Name of Contract : Construction of road embankment by earth filling & flexible pavement, surfacing with DBS wearing course(Asphalt overlay) & CC block protective work at 11th km(p), 12th km & 13th km(p) of Badherhat-Khairchar road under Road Division, Pabna/2010-2011

Contract Number : 24-PRC/Pab/2010-2011/WD-12

Name of Project : Badherghat - Khayerchar Road on Nagarbari Ferryghat (06150)

Budget Head : Development

Value of Contract : Tk.204,017,252.12(twenty crore forty lac seventeen thousand two hundred fifty-two taka and twelve paiza only)

Value of Work Done : TK. 203,610,468.60 (twenty crore thirty-six lac ten thousand four hundred sixty-eight taka and sixty paiza only)

Commencement Date : 16 June 2011

Planned Completion Date : 30 June 2014

Actual Completion Date : 28 June 2015

Signature of Engineer : *Haider* 27.7.16

Name of Engineer : (মোহাম্মদ হাইদার)

Designation of Engineer : নির্বাহী প্রকৌশলী (সি.এস.), সড়ক বিভাগ, পাবনা।

Date of Signature : \_\_\_\_\_

Seal of the Office : \_\_\_\_\_

Signature of Contractor : \_\_\_\_\_

*Mir Shariful Alam*  
Managing Director  
Dhrubo Construction Ltd.

Signed  
*AAM*  
কাজী আব্দুল আল-মামুন  
মোহাম্মদ  
সড়ক পরিবহন ও মর্যাদাপূর্ণক বিভাগ  
সড়ক পরিবহন ও সেতু মন্ত্রণালয়  
গণপ্রজাতন্ত্রী বাংলাদেশ সরকার





## Final Interim Payment Certificate

Office Name : Pabna, (Division Office)  
 Contract No : 24-PRC/Pab/2010-2011/WD-12  
 Contract Name : Construction of road embankment by earth filling & flexible pavement, surfacing with DBS wearing course (Asphalt overlay) & CC block protective work at 11th km(p), 12th km & 13th km(p) of Badherhat-Khairchar road under Road Division, Pabna/2010-2011  
 Budget Head : Development  
 Project Name : Badherghat - Khayerchar Road on Nagarbari Ferryghat (06150)  
 Contractor Name : Mir Shariful Alam & M/S. Dhrubo construction JV

Contract Value

Original Tk. : 204,017,252.12  
 Revised Tk. :

Start Date : 16 Jun, 2011

Completion Date

Planned : 15 Jun, 2013  
 Revised : 30 Jun, 2014  
 Actual : 28/06/2015

Interim Payment Certificate No. : 19F  
 Measurement upto : June 2014-15  
 Date of Measurement : 28-Jun-2015  
 Authorised Date :  
 Measurement Book Reference : M.B. No. 2309, 2489

	Cumulative Value	Previous Value upto 21/06/2015	Value of Works Since Last IPC
(A) Measurement (Value of Work Done )	203,610,468.60	202,914,216.85	696,251.75
(B) Retention 5.00 % of Contract Amount	(10,200,862.61)	(10,200,862.61)	(0.00)
(C) Total Value less Retention	193,409,605.99	192,713,354.24	696,251.75
(D) Amount due Prior to Advance and Tax	193,409,605.99	192,713,354.24	696,251.75

\* We certify that the works have been executed as per specification, drawing and terms & conditions of contract.

\* We certify that the quantity of works have been duly recorded in Measurement Books.

\* We certify that all materials used in the work satisfy the requirements of the specifications.

\* We certify that the value of works up to 28-Jun-2015 less retention is Taka Nineteen crore thirty-four lac nine thousand six hundred five taka and ninety-nine paisa only.

Prepared by: .....

Date: .....

Position held in RHD: SAE

Checked by: ..... E.R. to the Contract/ Other designation

Date: .....

Position held in RHD: EE, RHD, Pabna

Certified by: ..... Engineer to the Contract

Date: .....

Position held in RHD: SE, RHD, Pabna

Contractor: .....

Date: .....

Position: .....

Signed  
 AAF  
 কাজী আব্দুল আল-মামুন  
 যোগাযোগ  
 নতুন পরিদর্শন ও মহাসড়ক বিভাগ  
 নতুন পরিদর্শন ও সোহা মহাসড়ক  
 বাংলাদেশ সরকার



## Final Interim Payment Certificate

Office Name : Pabna, (Division Office)  
 Contract No : 24-PRC/Pab/2010-2011/WD-12  
 Contract Name : Construction of road embankment by earth filling & flexible pavement, surfacing with DBS wearing course (Asphalt overlay) & CC block protective work at 11th km(p), 12th km & 13th km(p) of Badherhat-Khairchar road under Road Division, Pabna/2010-2011  
 Budget Head : Development  
 Project Name : Badherhat - Khayerchar Road on Nagarbari Ferryghat (06150)  
 Contractor Name : Mir Shariful Alam & M/S. Dhrubo construction JV  
Contract Value  
 Original Tk. : 204,017,252.12  
 Revised Tk. :  
 Start Date : 16 Jun, 2011  
Completion Date  
 Planned : 15 Jun, 2013  
 Revised : 30 Jun, 2014  
 Actual : 28/06/2015

Interim Payment Certificate No. : 19F  
 Measurement upto : June 2014-15  
 Date of Measurement : 28-Jun-2015  
 Authorised Date :  
 Measurement Book Reference : M.B. No. 2309, 2489

## GRAND SUMMARY: BILL OF QUANTITIES:

Description	Contract Amount (in Taka)	Value of Work Done upto Previous Measure (in Taka)	Value of Work Done upto 28/06/2015 (in Taka)	% Completed
Division 1 - General & Site Facilities	2,404.00		2,404.00	100.00
Division 2 - Earthworks	47,528,082.99	46,586,413.44	47,268,620.94	99.45
Division 3 - Pavement Works	40,067,381.13	39,966,512.02	39,966,512.02	99.75
Division 5 - Structures	1,741,293.01	1,727,766.26	1,739,406.51	99.89
Division 6 - Incidentals	114,678,090.99	114,633,525.14	114,633,525.14	99.96
<b>Grand Total:</b>	<b>204,017,252.12</b>	<b>202,914,216.85</b>	<b>203,610,468.60</b>	<b>99.80</b>

Signed  
 AAM

কাজী আব্দুল আল-মামুন  
 যোগাযোগ  
 নতুন পরিদপ্তর ও মহাসড়ক বিভাগ  
 নতুন পরিদপ্তর ও সোহা মহাসড়ক  
 পাবনা-কাজী আব্দুল আল-মামুন





## Final Interim Payment Certificate

Office Name : Pabna, (Division Office)  
 Contract No : 24-PRC/Pab/2010-2011/WD-12  
 Contract Name : Construction of road embankment by earth filling & flexible pavement, surfacing with DBS wearing course (Asphalt overlay) & CC block protective work at 11th km(p), 12th km & 13th km(p) of Badherhat-Khairchar road under Road Division, Pabna/2010-2011  
 Budget Head : Development  
 Project Name : Badherghat - Khayerchar Road on Nagarbari Ferryghat (06150)  
 Contractor Name : Mir Shariful Alam & M/S. Dhrubo construction JV  
Contract Value  
 Original Tk. : 204,017,252.12  
 Revised Tk. :  
 Start Date : 16 Jun, 2011  
Completion Date  
 Planned : 15 Jun, 2013  
 Revised : 30 Jun, 2014  
 Actual : 28/06/2015

Interim Payment Certificate No. : 19F  
 Measurement upto : June 2014-15  
 Date of Measurement : 28-Jun-2015  
 Authorised Date :  
 Measurement Book Reference : M.B. No. 2309, 2489

## Bill Items Monthly Progress:

## Division 1 - General &amp; Site Facilities

Item Code	Item Description	Unit	Contract Qty	Unit Rate	Qty Done upto Prev. Measure	Qty Done upto 28/06/2015	Value of Work Done
01/02/04	Provision, Maintenance and Removal of Sign Boards	Lump Sum	1.0000	2,404.00		1.0000	2,404.00
Total Division 1 - General & Site Facilities Carried to Summary							2,404.00

## Division 2 - Earthworks

Item Code	Item Description	Unit	Contract Qty	Unit Rate	Qty Done upto Prev. Measure	Qty Done upto 28/06/2015	Value of Work Done
02/06/02	Embankment fill from borrow pit in contractor's Arranged land	cu metre	288,273.4950	150.00	282,067.7500	286,615.8000	42,992,370.00
02/07/02	Preparation of Subgrade 450 mm depth	sq. metre	17,366.7000	20.00	17,322.9000	17,322.9000	346,458.00
02/08/01	Improved Subgrade	cu metre	5,210.0000	570.00	5,196.8700	5,196.8700	2,962,215.90
02/10/01	Construction of Soil Earthen Shoulders	cu metre	7,886.3800	123.00	7,866.4800	7,866.4800	967,577.04
Total Division 2 - Earthworks Carried to Summary							47,268,620.94

Signed  
 AAM

কাজী আব্দুল আল-মামুন  
 যোগাযোগ  
 নথি পরিচালক ও মহাপ্রকল্প পরিচালক  
 নথি পরিচালক ও সচিব মহাপ্রকল্প  
 বাংলাদেশ সরকার



## Final Interim Payment Certificate

Office Name : Pabna, (Division Office)  
 Contract No : 24-PRC/Pab/2010-2011/WD-12  
 Contract Name : Construction of road embankment by earth filling & flexible pavement, surfacing with DBS wearing course (Asphalt overlay) & CC block protective work at 11th km(p), 12th km & 13th km(p) of Badherhat-Khairchar road under Road Division, Pabna/2010-2011  
 Budget Head : Development  
 Project Name : Badherghat - Khayerchar Road on Nagarbari Ferryghat (06150)  
 Contractor Name : Mir Shariful Alam & M/S. Dhrubo construction JV  
 Contract Value

Original Tk. : 204,017,252.12  
 Revised Tk. :

Start Date : 16 Jun, 2011

## Completion Date

Planned : 15 Jun, 2013  
 Revised : 30 Jun, 2014  
 Actual : 28/06/2015

Interim Payment Certificate No. : 19F  
 Measurement upto : June 2014-15  
 Date of Measurement : 28-Jun-2015  
 Authorised Date :  
 Measurement Book Reference : M.B. No. 2309, 2489

## Division 3 - Pavement Works

Item Code	Item Description	Unit	Contract Qty	Unit Rate	Qty Done upto Prev. Measure	Qty Done upto 28/06/2015	Value of Work Done
03/02/01	Sub-Base	cu metre	4,341.6700	2,800.00	4,330.7250	4,330.7250	12,126,030.00
03/03/01	Aggregate Base Type I	cu metre	2,605.0000	3,389.00	2,598.4400	2,598.4400	8,806,113.16
03/03/02	Aggregate Base Type II	cu metre	2,605.0000	2,683.00	2,598.4350	2,598.4350	6,971,601.11
03/06/01a	Bituminous Prime Coat (Plant Placed)	sq. metre	17,366.7000	69.00	17,322.9000	17,322.9000	1,195,280.10
03/10/02b	DBS - Wearing Course 50mm thick (Av.)	cu metre	868.3300	12,251.00	866.1500	866.1500	10,611,203.65
03/13/01	Brick on End Edging	Lin. Metre	4,758.0000	54.00	4,746.0000	4,746.0000	256,284.00
Total Division 3 - Pavement Works Carried to Summary							39,966,512.02

## Division 5 - Structures

Item Code	Item Description	Unit	Contract Qty	Unit Rate	Qty Done upto Prev. Measure	Qty Done upto 28/06/2015	Value of Work Done
05/01/02a	Concrete Class as Detailed on Drawings ( Class10)	cu metre	379.1300	4,562.00	378.7300	378.7300	1,727,766.26
05/01/02b	Concrete class-20 (Foundation)	cu metre	1.0800	6,836.00		1.0800	7,382.88
05/02/01	Mild Steel Reinforcement Bars	Tonne	0.0700	61,701.00		0.0690	4,257.37
Total Division 5 - Structures Carried to Summary							1,739,406.51

Signed  
 AAM

কাজী আব্দুল আল-মামুন  
 যোগাযোগ  
 নতুন পরিদপন ও মহাসড়ক বিভাগ  
 নতুন পরিদপন ও সেতু মহালয়  
 গণপ্রজাতন্ত্রী বাংলাদেশ সরকার





## Final Interim Payment Certificate

Office Name : Pabna, (Division Office)  
 Contract No. : 24-PRG/Pab/2010-2011/WD-12  
 Contract Name : Construction of road embankment by earth filling & flexible pavement, surfacing with DBS wearing course (Asphalt overlay) & CC block protective work at 11th km(p), 12th km & 13th km(p) of Badherhat-Khairchar road under Road Division, Pabna/2010-2011  
 Budget Head : Development  
 Project Name : Badherghat - Khayerchar Road on Nagarbari Ferryghat (06150)  
 Contractor Name : Mir Shariful Alam & M/S. Dhruvo construction JV

## Contract Value

Original Tk. : 204,017,252.12  
 Revised Tk. :

Start Date : 16 Jun, 2011

## Completion Date

Planned : 15 Jun, 2013  
 Revised : 30 Jun, 2014  
 Actual : 28/06/2015

Interim Payment Certificate No. : 19F  
 Measurement upto : June 2014-15  
 Date of Measurement : 28-Jun-2015  
 Authorised Date :  
 Measurement Book Reference : M.B. No. 2309, 2489

## Division 5 - Incidentals

Item Code	Item Description	Unit	Contract Qty	Unit Rate	Qty Done upto Prev. Measure	Qty Done upto 28/06/2015	Value of Work Done
06/05/01	Road Marking - Thermoplastic Material (indicate if screed or spray application)	Sq Metre	630.6400	848.00	630.6000	630.6000	534,748.80
06/10/01	Traffic Signs	Number	8.0000	4,205.00	8.0000	8.0000	33,640.00
06/10/02	Sign Post	Number	26.0000	1,995.00	26.0000	26.0000	51,870.00
06/11/01	Rumble strips (Bituminous Concrete Volume)	cu metre	80,582.0000	117.00	80,582.0000	80,582.0000	9,428,094.00
06/01/02a (Special)	Concrete slope protection CC block Size 450x450x200 etc. complete	Nos.	178,983.0000	219.00	178,780.0000	178,780.0000	39,152,820.00
06/01/02c (Special)	Concrete slope protection C.C. block size 450mm.x450mm.x300mm.	Nos.	178,983.0000	326.00	178,983.0000	178,983.0000	58,348,458.00
Special Item 06(a) (Labour charge for laying CC Block	Labour charge for laying CC Block (Block size 450mm.x450mm.x200mm.)	Nos.	178,983.0000	21.50	178,983.0000	178,983.0000	3,848,134.50
Special Item 100mm bedding layer with khoa	100mm bedding layer with khoa >20mm size over 3.00mm thick Geotextile	Cum	6,921.0800	32.30	6,918.7600	6,918.7600	223,475.95
Special Item No. 06(c) (Labour charge for laying CC block	Labour charge for laying CC block (size 450mmx450mmx300mm)	Nos.	178,983.0000	16.83	178,983.0000	178,983.0000	3,012,283.89

Total Division 5 - Incidentals Carried to Summary

Signed  
  
 কাজী আব্দুল আল-মামুন  
 যোগাযোগ  
 নথি পরিচালনা ও মহাপ্রকল্প বিভাগ  
 সড়ক পরিবহন ও সেতু মন্ত্রণালয়  
 গণপ্রজাতন্ত্রী বাংলাদেশ সরকার



## Final Interim Payment Certificate

Office Name : Pabna, (Division Office)  
 Contract No : 24-PRC/Pab/2010-2011/WD-12  
 Contract Name : Construction of road embankment by earth filling & flexible pavement, surfacing with DBS wearing course (Asphalt overlay) & CC block protective work at 11th km(p), 12th km & 13th km(p) of Badherhat-Khairchar road under Road Division, Pabna/2010-2011  
 Budget Head : Development  
 Project Name : Badherghat - Khayerchar Road on Nagarbari Ferryghat (06150)  
 Contractor Name : Mir Shariful Alam & M/S. Dhrubo construction JV  
Contract Value  
 Original Tk. : 204,017,252.12  
 Revised Tk. :  
 Start Date : 16 Jun, 2011  
Completion Date  
 Planned : 15 Jun, 2013  
 Revised : 30 Jun, 2014  
 Actual : 28/06/2015

Interim Payment Certificate No. : 19F  
 Measurement upto : June 2014-15  
 Date of Measurement : 28-Jun-2015  
 Authorised Date :  
 Measurement Book Reference : M.B. No. 2309, 2489

Total Amount:

203,610,468.60

Words: Twenty crore thirty-six lac ten thousand four hundred sixty-eight taka and sixty paise only

Signed  
 AAM  
 কাজী আব্দুল্লাহ আল-মামুন  
 যোগাযোগ  
 নথি পরিচালনা ও মহাসড়ক বিভাগ  
 সড়ক পরিবহন ও সেতু মন্ত্রণালয়  
 গণপ্রজাতন্ত্রী বাংলাদেশ সরকার





## Final Interim Payment Certificate

Office Name : Pabna, (Division Office)  
 Contract No : 24-PRC/Pab/2010-2011/WD-12  
 Contract Name : Construction of road embankment by earth filling & flexible pavement, surfacing with DBS wearing course (Asphalt overlay) & CC block protective work at 11th km(p), 12th km & 13th km(p) of Badherhat-Khairchar road under Road Division, Pabna/2010-2011  
 Budget Head : Development  
 Project Name : Badherghat - Khayerchar Road on Nagarbari Ferryghat (06150)  
 Contractor Name : Mir Shariful Alam & M/S. Dhruvo construction JV  
Contract Value  
 Original Tk. : 204,017,252.12  
 Revised Tk. :  
 Start Date : 16 Jun, 2011  
Completion Date  
 Planned : 15 Jun, 2013  
 Revised : 30 Jun, 2014  
 Actual : 28/06/2015

Interim Payment Certificate No. : 19F  
 Measurement upto : June 2014-15  
 Date of Measurement : 28-Jun-2015  
 Authorised Date :  
 Measurement Book Reference : M.B. No. 2309, 2489

Engineer's Representatives Report:

## Performance on Quality of Work including Testing

Prepared by: ..... E.R. to the Contract/ Other designation Date: .....

Position held in RHD: EE, RHD, Pabna

Engineer's Report:

## Comments on Engineer's Representative Report

Prepared by: ..... Engineer to the Contract Date: .....

Position held in RHD: SE, RHD, Pabna

Signed  
 AAM

কাজী আব্দুল আল-মামুন  
 যোগাযোগ  
 নতুন পরিদর্শন ও মহাসড়ক বিভাগ  
 নতুন পরিদর্শন ও সেতু মহাপ্রকল্প  
 বাংলাদেশ সরকার




## Final Interim Payment Certificate

Office Name : Pabna, (Division Office)  
 Contract No : 24-PRC/Pab/2010-2011/WD-12  
 Contract Name : Construction of road embankment by earth filling & flexible pavement, surfacing with DBS wearing course (Asphalt overlay) & CC block protective work at 11th km(p), 12th km & 13th km(p) of Badherhat-Khairchar road under Road Division, Pabna/2010-2011  
 Budget Head : Development  
 Project Name : Badherghat - Khayerchar Road on Nagarbari Ferryghat (06150)  
 Contractor Name : Mir Shariful Alam & M/S. Dhruvo construction JV  
 Contract Value :  
     Original Tk. : 204,017,252.12  
     Revised Tk. :  
 Start Date : 16 Jun, 2011  
 Completion Date :  
     Planned : 15 Jun, 2013  
     Revised : 30 Jun, 2014  
     Actual : 28/06/2015

Interim Payment Certificate No. : 19F  
 Measurement upto : June 2014-15  
 Date of Measurement : 28-Jun-2015  
 Authorised Date :  
 Measurement Book Reference : M.B. No. 2309, 2489

## Contract Plan:

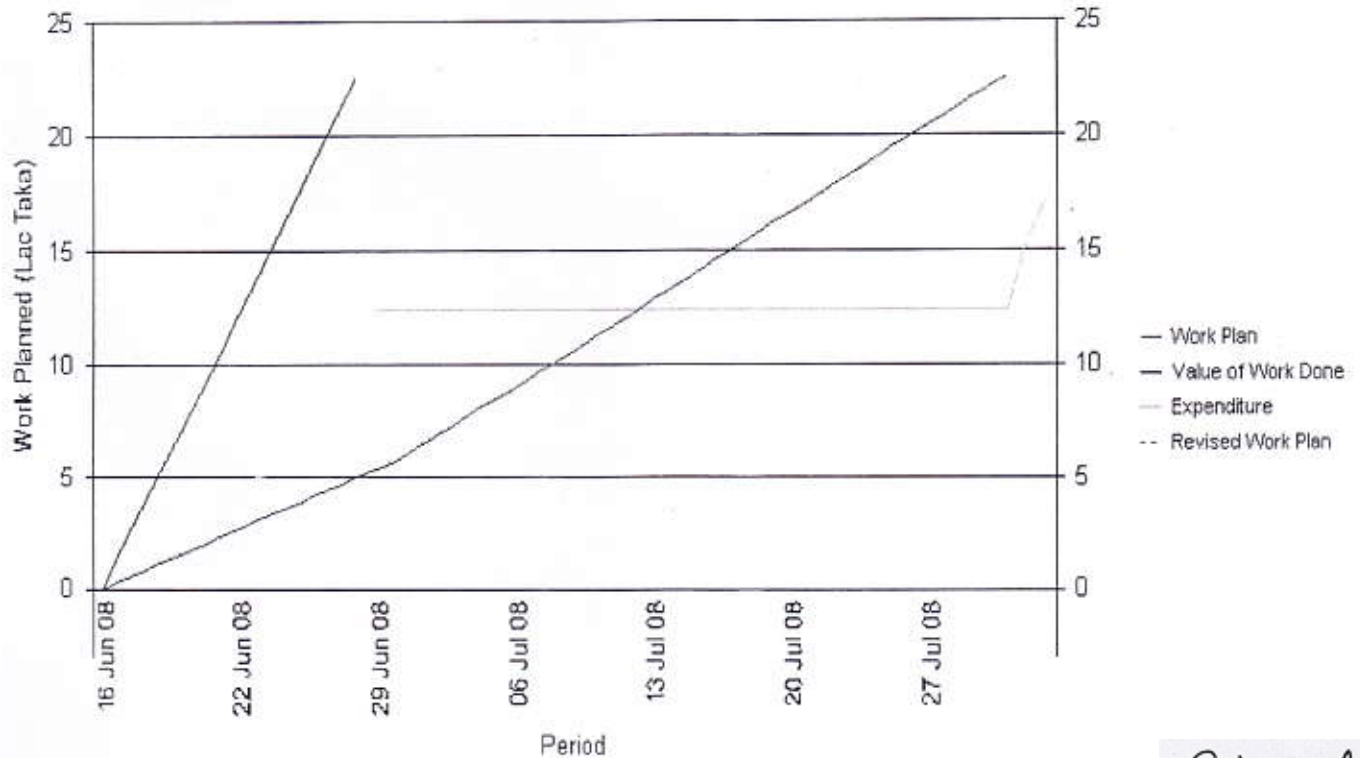

Signed  
 AAM

কাজী আব্দুল আল-মামুন  
 প্রোগ্রামার  
 নতুন পরিচালন ও মালিকানা বিভাগ  
 নতুন পরিচালন ও সেবা মন্ত্রণালয়  
 গণপ্রজাতন্ত্রী বাংলাদেশ সরকার
